


# Foundation/Basement Detail for Modular or Mobile Home

All Mobile Homes must be H.U.D. Approved and Labeled.

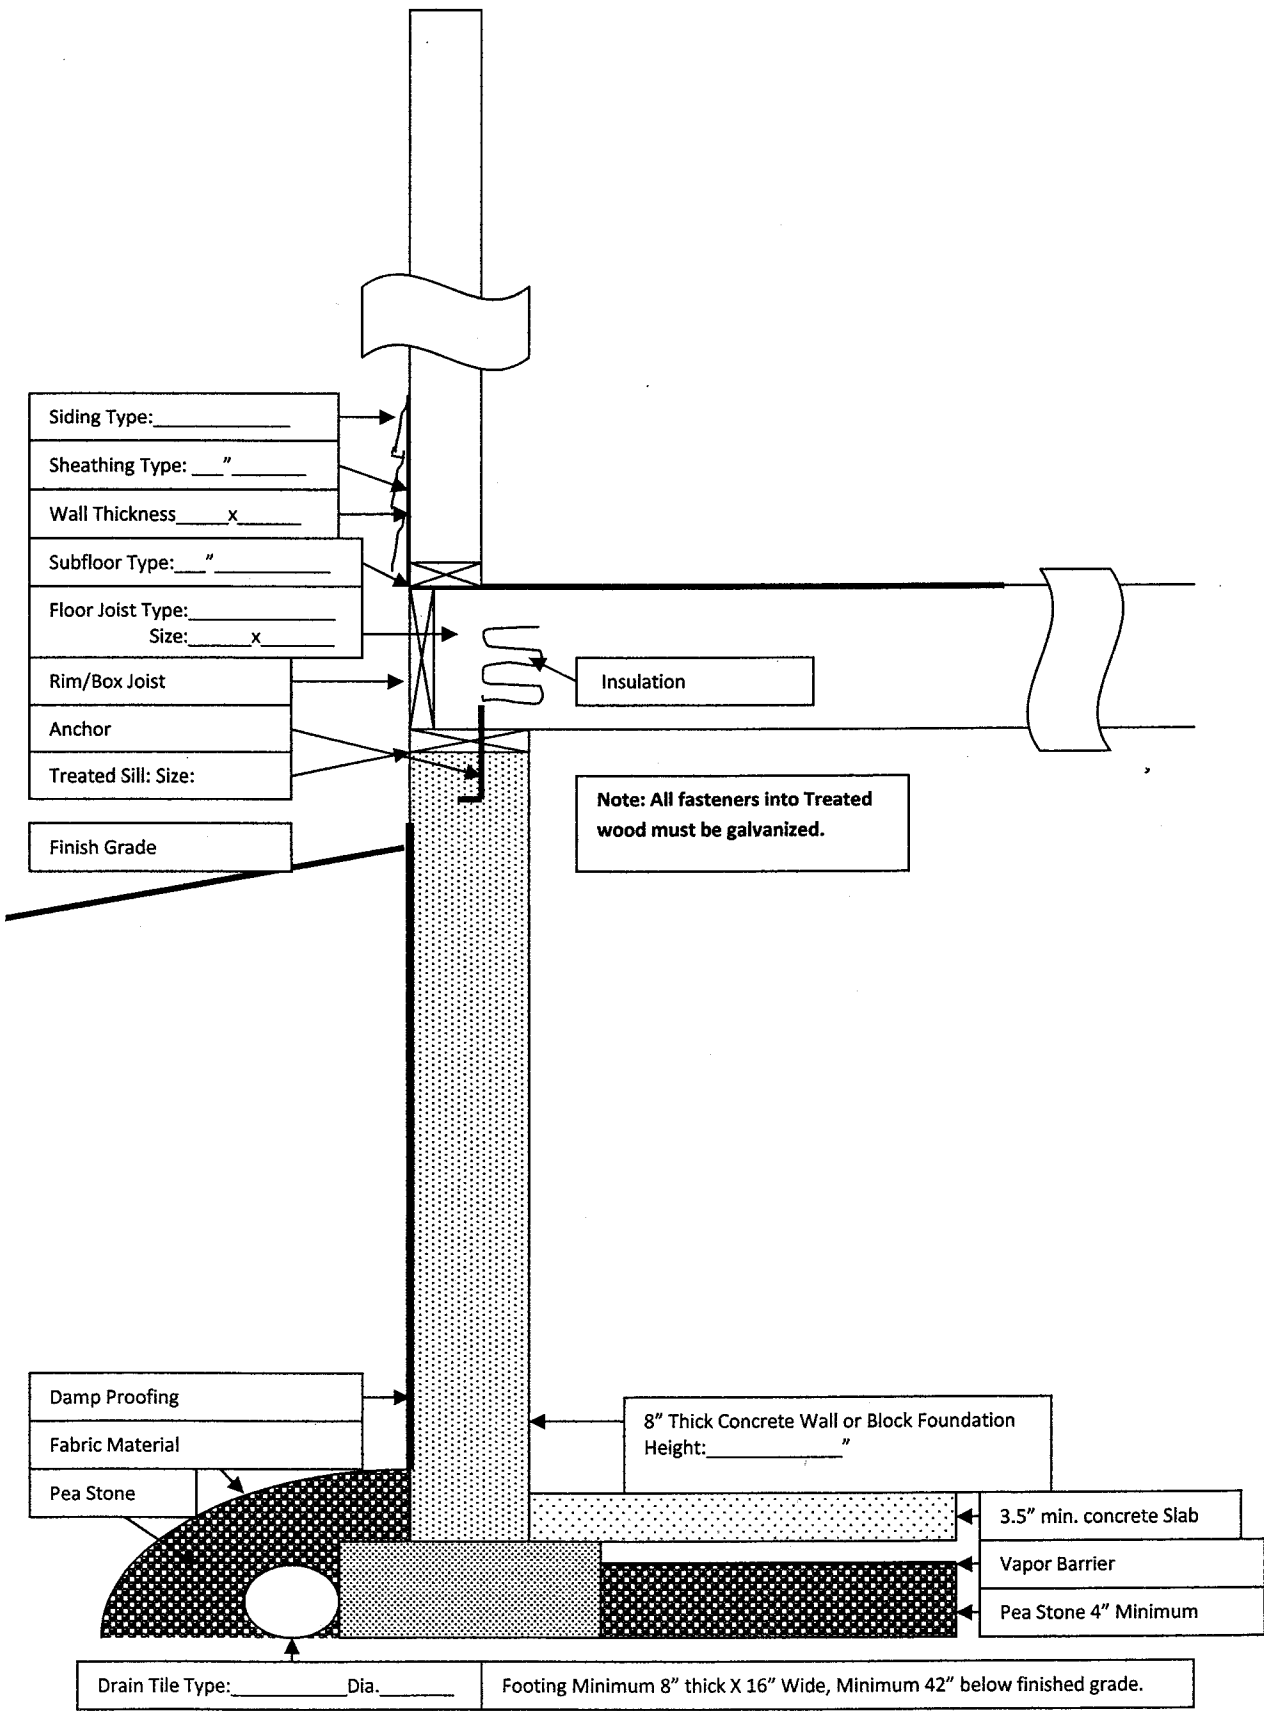

Siding Type: \_\_\_\_\_

Sheathing Type: \_\_\_\_\_"

Wall Thickness \_\_\_\_\_ x \_\_\_\_\_

Subfloor Type: \_\_\_\_\_"

Floor Joist Type: \_\_\_\_\_  
Size: \_\_\_\_\_ x \_\_\_\_\_

Rim/Box Joist

Anchor

Treated Sill: Size: \_\_\_\_\_

Finish Grade

Damp Proofing

Fabric Material

Pea Stone

Drain Tile Type: \_\_\_\_\_ Dia. \_\_\_\_\_

Footing Minimum 8" thick X 16" Wide, Minimum 42" below finished grade.

Insulation

**Note: All fasteners into Treated wood must be galvanized.**

**8" Thick Concrete Wall or Block Foundation  
Height: \_\_\_\_\_"**

**3.5" min. concrete Slab**

**Vapor Barrier**

**Pea Stone 4" Minimum**
